



WEST VALLEY CONNECTOR


**Board of Directors
November 6, 2024**



ROLES/RESPONSIBILITIES


OmniTrans

- Small Starts grant recipient
- Leading bus build and construction of maintenance facility upgrades
- Owner / Operator
- Maintenance of stations and transit signal priority

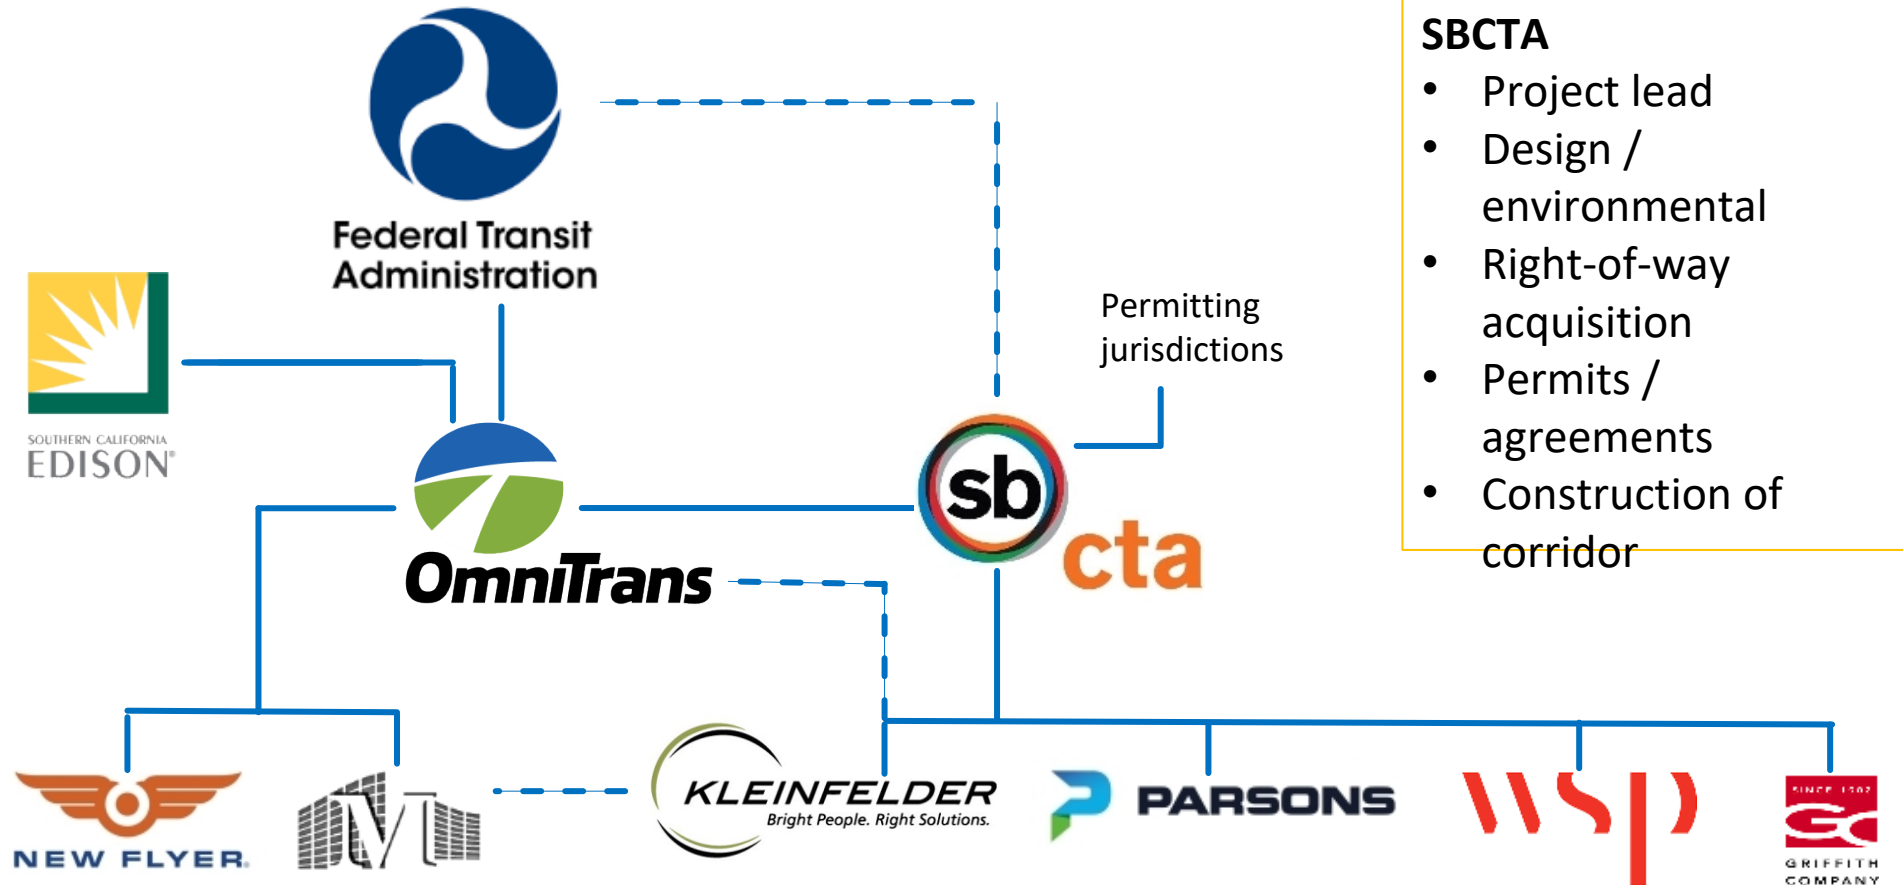

Accomplishments/Highlights


- Corridor construction – street light / traffic signal improvements, utility relocation, and concrete flatwork
 - 9.1% complete as of 9/12
- Construction at Pomona Transit Center continues to install in-route charging
- Started side running station construction (Pomona & Montclair)

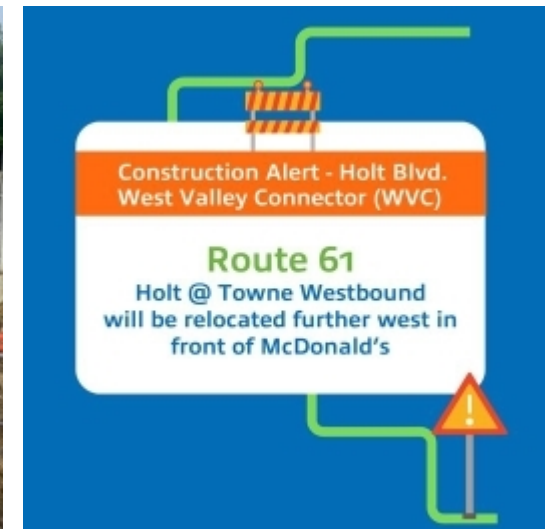

Corridor Construction along Holt

Accomplishments/Highlights

- Remaining buses are expected to enter line production Oct 28th
- West Valley Facility construction to begin April or May 2025
 - Currently working with Edison for utility coordination at WV Facility
 - Metro Builders has ordered long lead items for WV charge canopy
- Second quarterly in-person meeting with FTA

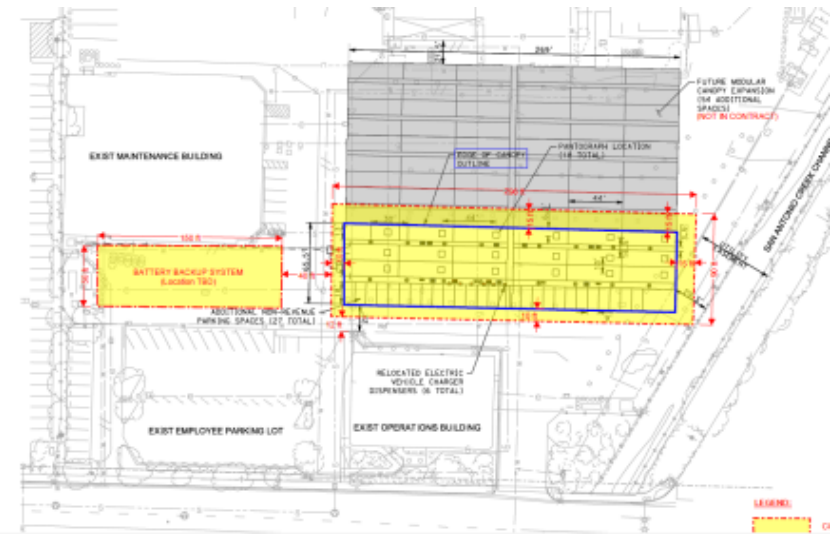

SCHEDULE

SBCTA Activities	Expected Date
Testing/commissioning	Fall 2026
Substantial completion of mainline corridor	December 2026
Start Revenue Service	December 2026

OmniTrans Activities	Expected Date
Receive remaining 16 buses (Begin production Oct. 2024)	March 2025
Complete construction of maintenance facility upgrades	April 2026
Start revenue service	December 2026



THANK YOU
